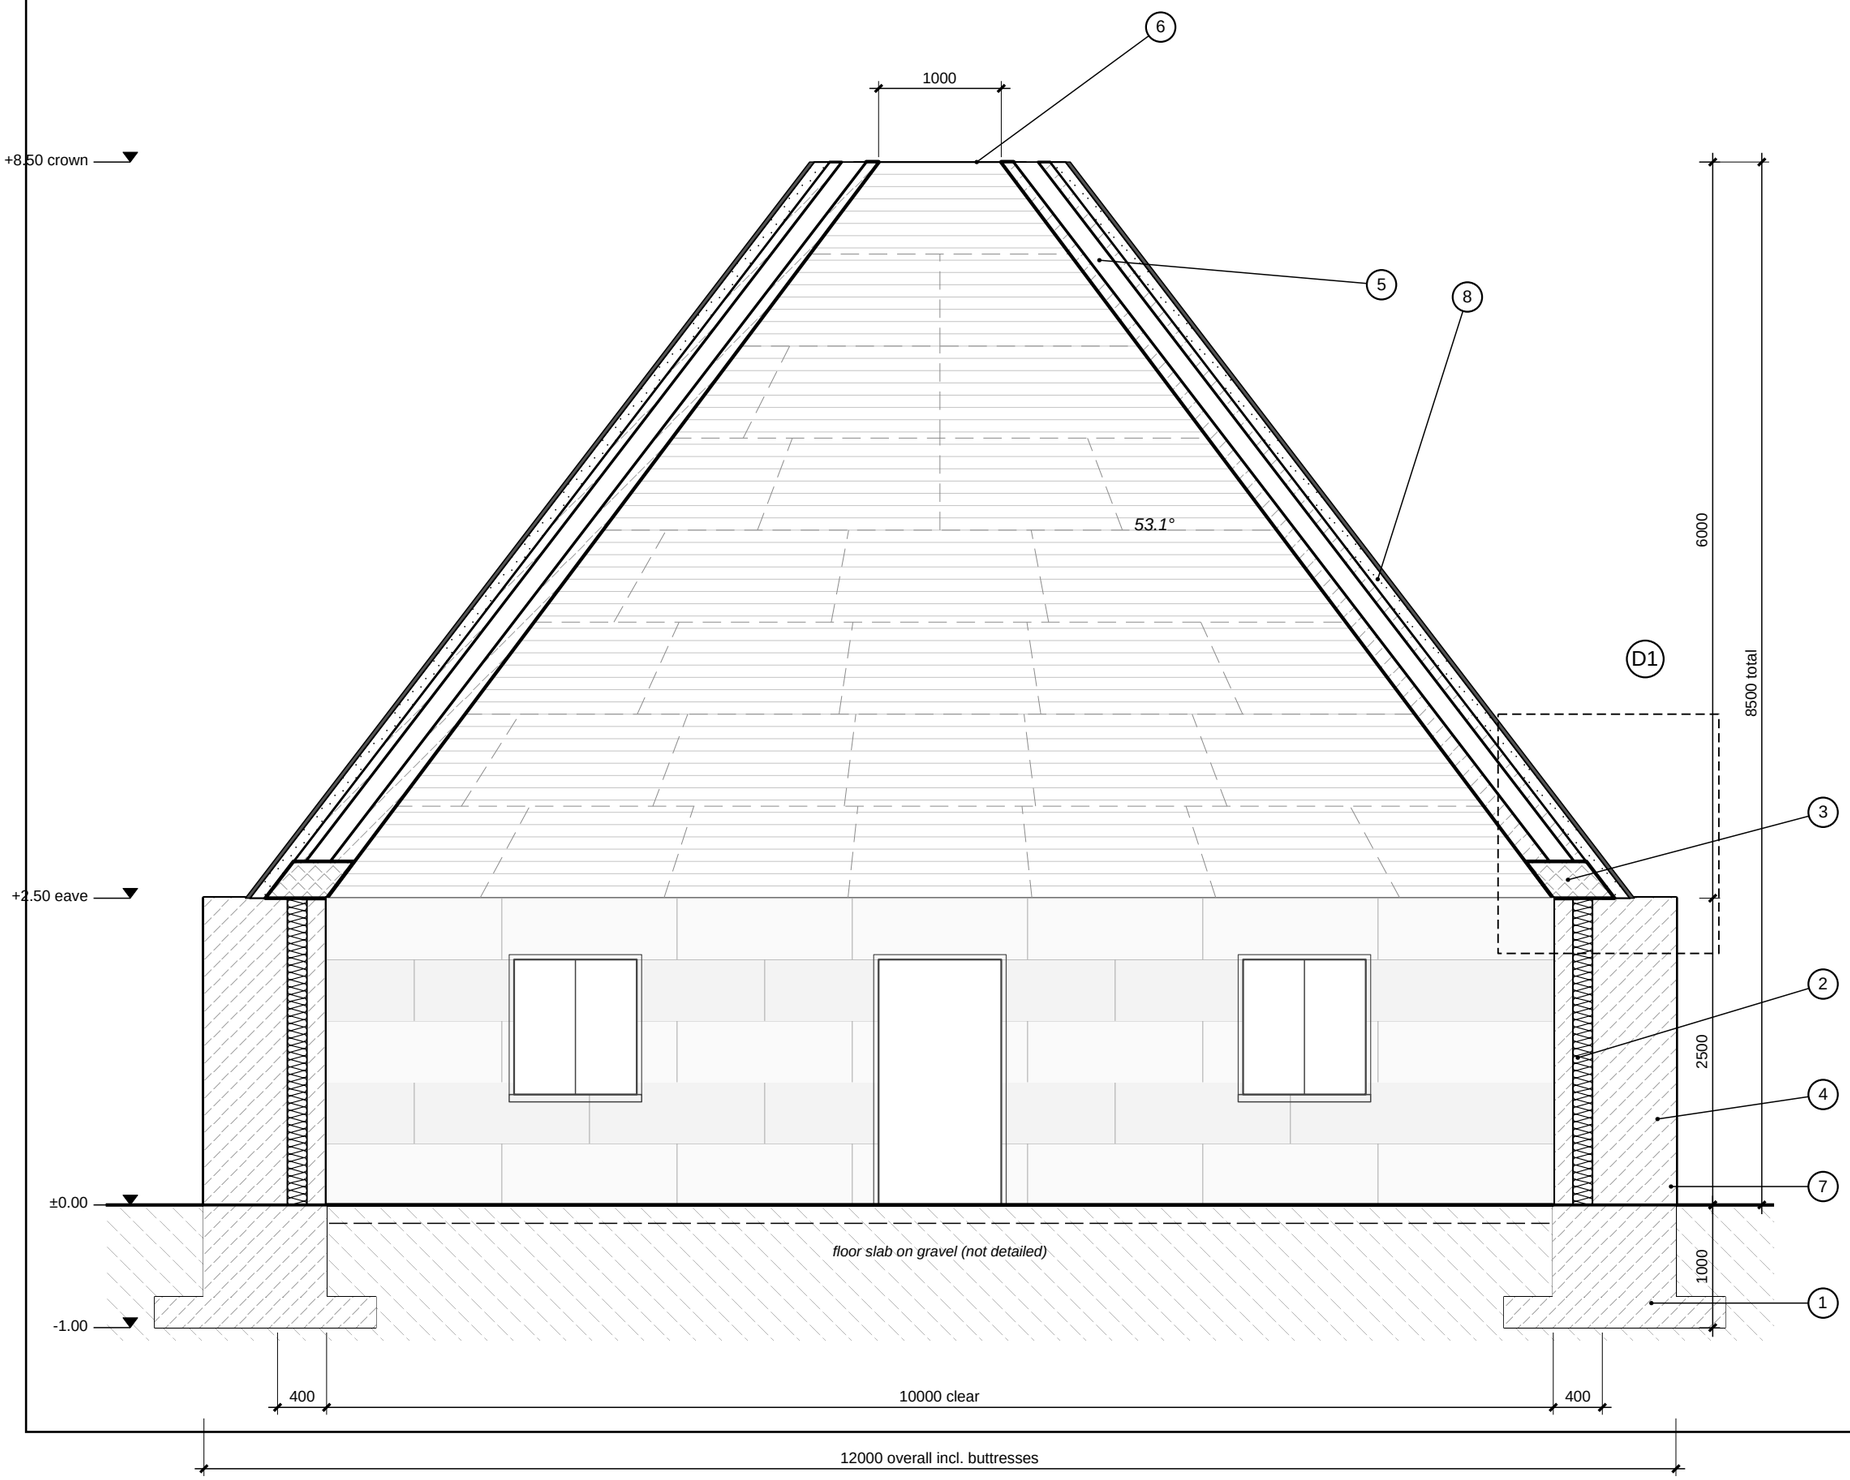


Total section A-A

through the east and west buttresses, looking north

1. Footing 1800 x 250, underside at -1000 (frost depth and bearing are guesses).
2. Printed wall 400, same pattern as the roof: two 80 inner layers, a 160 air zone, an 80 outer layer.
3. Solid base of the roof: the first 300 (vertical) above the eave is completely solid concrete, 400 wide, no air zone; there is no ring beam.
4. Buttress 400 wide, 1000 from the inner face (600 beyond the wall), one about every 1.5 m (8 per side); it rises to +2.50, flush with the roof base.
5. Roof shell: 400 thick square to the slope at the base (two 80 inner layers, a 160 air zone, an 80 outer layer), 320 at the crown; about 500 / 400 horizontally.
6. Crown opening 1000 clear; roof rises 6000 over 4500, slope 53.1° (36.9° from the vertical).
7. Everything is 3D printed in 10 mm layers; crossed hatch = solid cast concrete (roof base, ribs). Printed layer joints and the cast fill of the buttress and footing are shown in the roof-grid sheets and in detail D1.
8. Outside the printed shell: insulation 100 (dotted), then the outer layer (cladding 30, dark).
9. Cast ribs of the roof grid, seen on the back face as dashed outlines (no roof grid shown). The cut lies in the air zone between ribs; rib sections are on the roof-grid sheets.

● from your sketches
○ assumed by me, to confirm

Notes

Layer pattern from your drawing; at the crown the second inner layer ends, so the leaf is 80 there (assumed).

The cut runs through the 4th buttress from the south (y = -743); the north wall with its door and windows is seen beyond.

Faint grid on the back roof face and the north wall = printed pieces in running bond, about 1500 wide (assumed sizes). Dashed outlines on the back roof face = cast ribs.

0 1 2 3 4 5 m

Scale 1:50 at A3 · dimensions in mm · draft 1, 2026-10-11
pyramid-roof · hand estimates, not engineered
