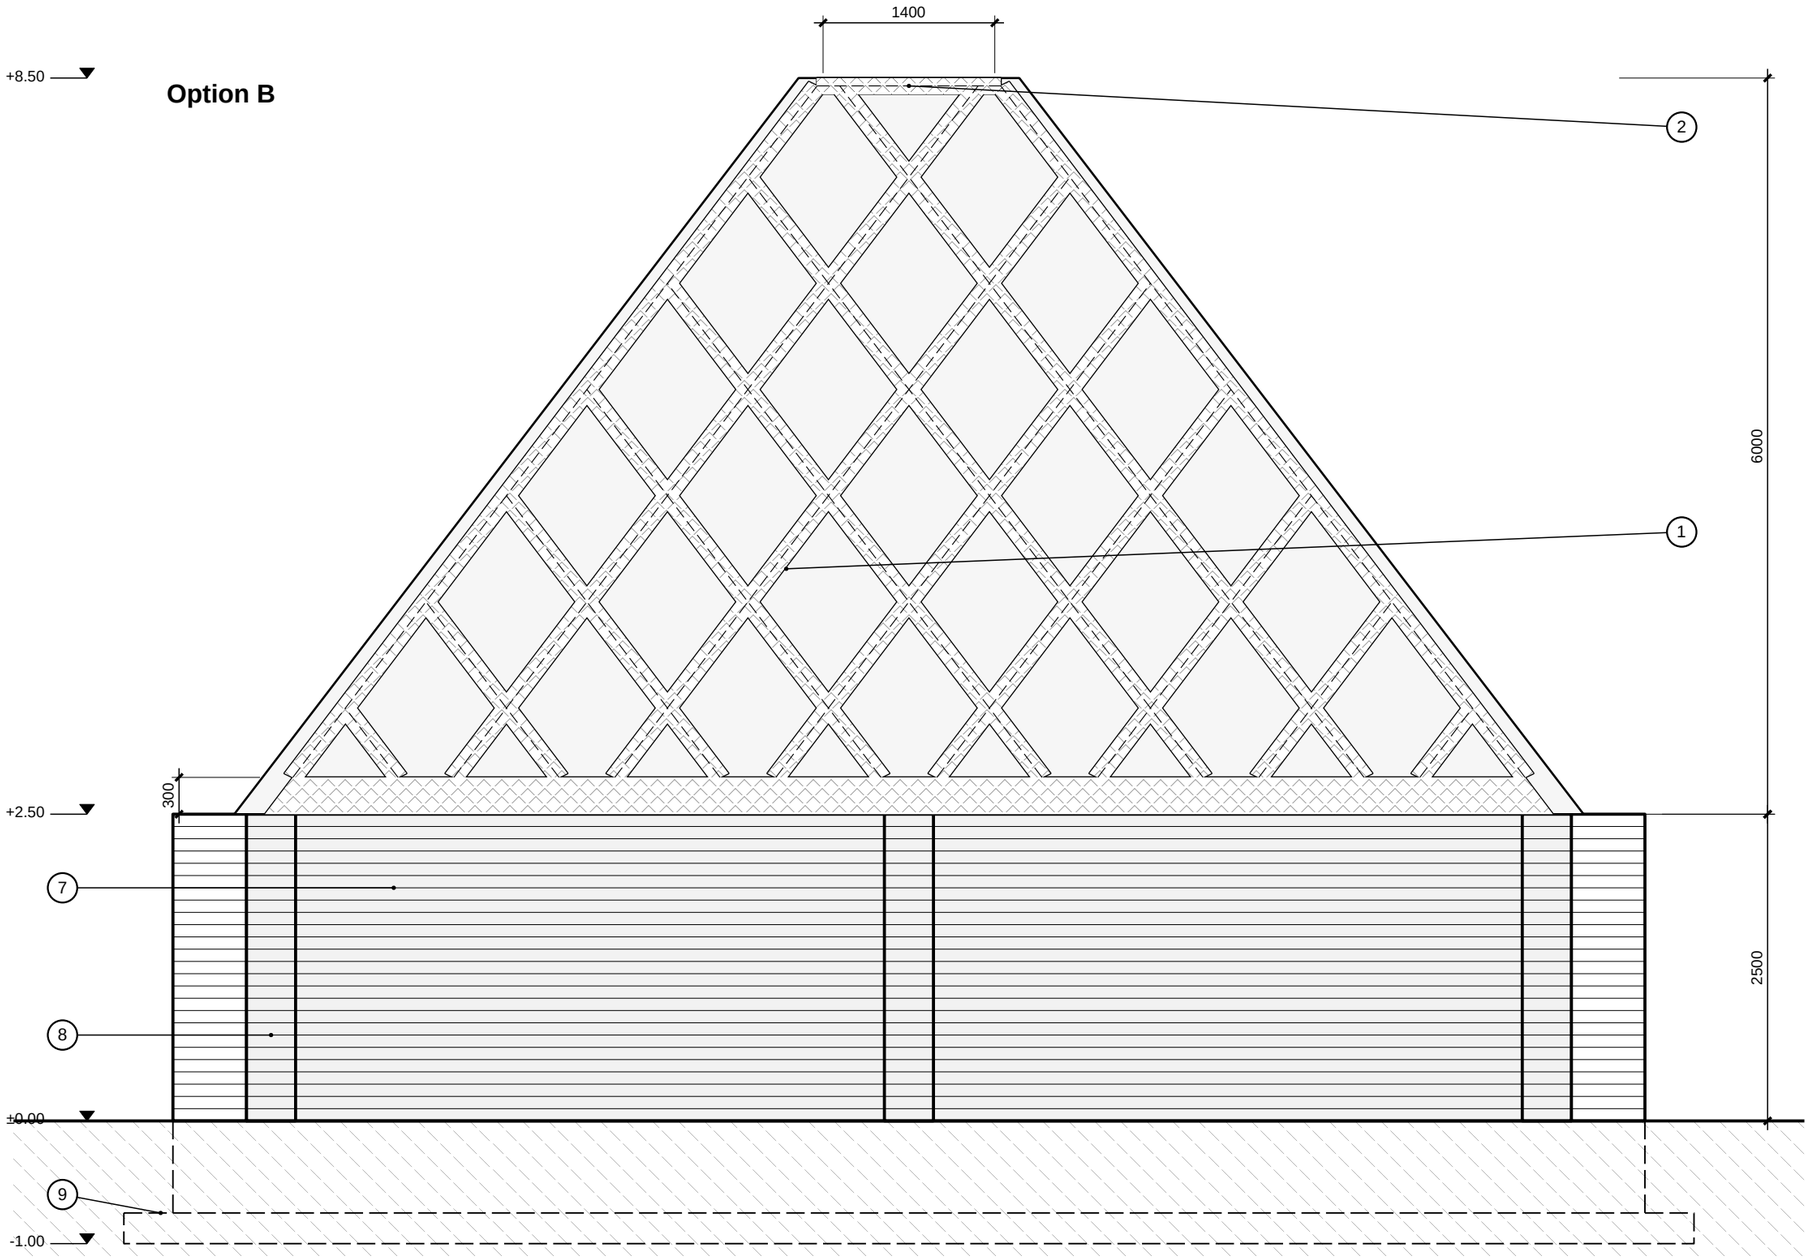

Section through one rib, square to the slope, 1:10

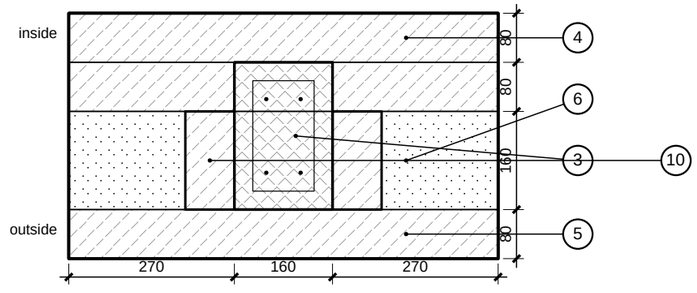

Roof grid B: diamond lattice

one roof face seen square on

(1) Diagonals parallel to the two hips (same inclination as the roof edges, 58.9° in the face), every 1312.5 along the base: equal diamonds 1312.5 wide.

(2) Bottom ring = the 300 solid base; top ring at the crown. The hips are two of the diagonals. No other horizontal ribs.

(3*) Rib (column): a channel 160 wide x 240 deep printed in the 160 air zone + layer 2 stays in place as formwork and is filled with cast concrete, 4 Ø16 + Ø8 stirrups every 200 (assumed). Fibre concrete could replace the bars (see notes).

(4) Inner layer 1, 80: continuous, covers the grid on the room side.

(5) Outer skin 80: continuous, covers the grid on the outside (cladding on it).

(6*) Between the ribs the air zone stays open for thermal insulation (dotted).

(7) Printed wall 400 (same layers as the roof), to +2.50.

(8) Buttresses 400 wide, 1000 from the inner face (600 outside), at the corners and mid-span; roof ribs and wall bars tie into the solid base above them.

(9*) Strip footing 1800 x 250, underside at -1.00 (hidden, dashed): printed edge formwork, cast core.

(10) Printed channel walls, 80 each side of the rib: permanent formwork, printed in the same pass as the shell.

* = assumed, to confirm

Notes

Every diagonal ends on a ring or on a hip, so no bar has a free end in the shell.

Diagonals do not stop as the roof narrows: the diamonds just get clipped by the hips.

All 3D printed (after the Obayashi 3dpod paper, 2023): mortar beads are printed as permanent formwork, in 10 mm layers (joints drawn every 100 on the elevation), and the structural concrete is cast into them in lifts limited by formwork pressure; the shell, wall and buttress faces are the printed skin.

The paper fills the formwork with self-compacting steel-fibre UHPC (about 180 N/mm2 compression, 8.8 tension) and needs no rebar in principle; if you use it, the Ø16 bars in the ribs can be dropped or cut back, to be confirmed with the engineer.

Rough quantities, four faces (hips counted twice, so slightly high): ribs 330 m, 4 Ø16 each bars, steel 2085 kg, cast concrete 12.7 m3.

Rib size, bar count and the 160 x 240 channel are assumptions for the engineer to check. Elevation shows the face square on; true lengths are 1.25 x the drawn heights.

0 1 2 3 4 5 m

Scale 1:50 at A3 · dimensions in mm · draft 1, 2026-10-11
pyramid-roof · hand estimates, not engineered
