
Total section A-A · grid A

through the east and west buttresses, looking north

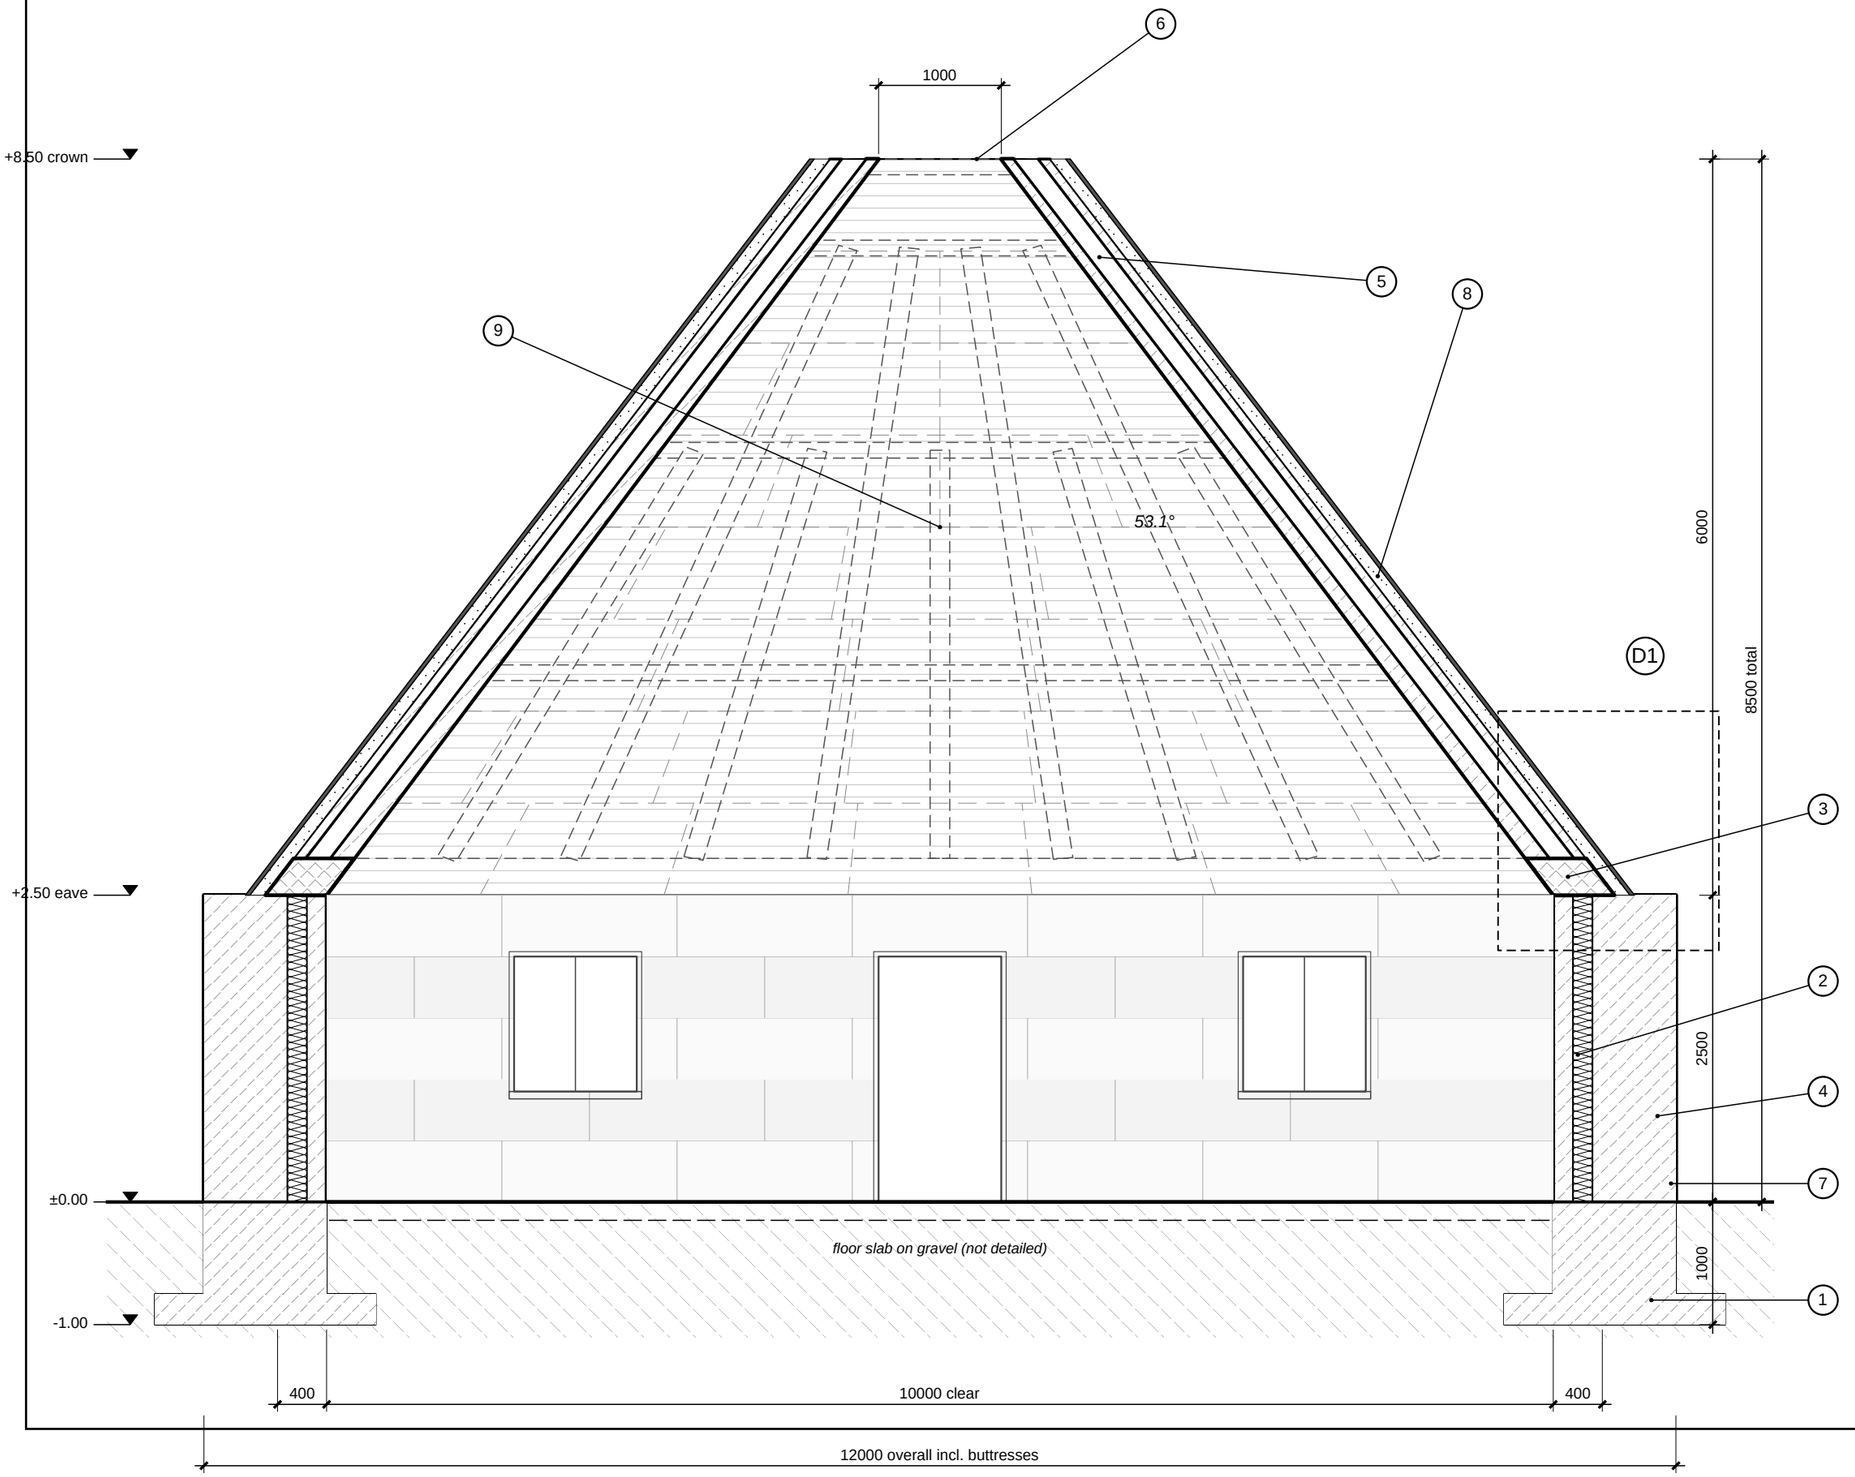

1. Footing 1800 x 250, underside at -1000 (frost depth and bearing are guesses).
2. Printed wall 400, same pattern as the roof: two 80 inner layers, a 160 air zone, an 80 outer layer.
3. Solid base of the roof: the first 300 (vertical) above the eave is completely solid concrete, 400 wide, no air zone; there is no ring beam.
4. Buttress 400 wide, 1000 from the inner face (600 beyond the wall), one about every 1.5 m (8 per side); it rises to +2.50, flush with the roof base.
5. Roof shell: 400 thick square to the slope at the base (two 80 inner layers, a 160 air zone, an 80 outer layer), 320 at the crown; about 500 / 400 horizontally.
6. Crown opening 1000 clear; roof rises 6000 over 4500, slope 53.1° (36.9° from the vertical).
7. Everything is 3D printed in 10 mm layers; crossed hatch = solid cast concrete (roof base, ribs). Printed layer joints and the cast fill of the buttress and footing are shown in the roof-grid sheets and in detail D1.
8. Outside the printed shell: insulation 100 (dotted), then the outer layer (cladding 30, dark).
9. Cast ribs of the roof grid, seen on the back face as dashed outlines (roof grid A, ruled-surface columns). The cut lies in the air zone between ribs; rib sections are on the roof-grid sheets.

● from your sketches
○ assumed by me, to confirm

Notes

Layer pattern from your drawing; at the crown the second inner layer ends, so the leaf is 80 there (assumed).

The cut runs through the 4th buttress from the south (y = -743); the north wall with its door and windows is seen beyond.

Faint grid on the back roof face and the north wall = printed pieces in running bond, about 1500 wide (assumed sizes). Dashed outlines on the back roof face = cast ribs.

0 1 2 3 4 5 m

Scale 1:50 at A3 · dimensions in mm · draft 1, 2026-10-11
pyramid-roof · hand estimates, not engineered
